


ID	Task Name	Duration	Start	Finish	Predecessors	May '11		Jun '11			Jul '11			Aug '11			Sep '11			Oct '11							
						17	24	1	8	15	22	29	5	12	19	26	3	10	17	24	31	7	14	21	28	4	11
1	Shinn Real Estate Exchange (REE, former Purchase and Sale A	141 days	Tue 4/26/11	Tue 11/15/11																							
2	Define New Road Alignment (Both Parties in Agreement)	8 days	Tue 4/26/11	Thu 5/5/11																							
3	Acquire Preliminary Title Report	9 days	Fri 5/6/11	Wed 5/18/11	2																						
4	Survey Property - Tie Existing Points	0 days	Thu 4/28/11	Thu 4/28/11	2																						
5	Establish Datum - Records Research and Review Preliminary T	0 days	Wed 5/4/11	Wed 5/4/11	4,3																						
6	Prepare Legal Descriptions/Exhibits - Road & PUE, Slope, TCE	15 days	Wed 5/4/11	Tue 5/24/11	5																						
7	Prepare Draft PSAA	15 days	Fri 5/6/11	Thu 5/26/11	2,6																						
8	County Counsel Draft REE (PSAA) Review/Approve	53 days	Tue 7/19/11	Fri 9/30/11	7																						
9	Negotiate REE (PSAA)	15 days	Mon 10/3/11	Mon 10/24/11	8																						
10	County Counsel Blue Review	5 days	Tue 10/25/11	Mon 10/31/11	9																						
11	BOS Approval of REE (PSAA) (includes Registrar and Approval	10 days	Tue 11/1/11	Tue 11/15/11	10																						
12	Architectural Services Agreement Amendment (ASAA)	133 days	Fri 5/6/11	Tue 11/15/11																							
13	Define Phase 1 Scope of Work - Consistent w/ Shinn PSAA	5 days	Fri 5/6/11	Thu 5/12/11	2																						
14	Prepare and Process a Contract Assignment Agreement	18 days	Fri 7/15/11	Tue 8/9/11	13																						
15	Request Proposal of Amendment Services (Cost & Proposed S	25 days	Wed 8/10/11	Wed 9/14/11	14																						
16	Prepare ASAA	14 days	Sun 9/4/11	Fri 9/23/11	15																						
17	Contract Services Officer ASAA Review/Approve	5 days	Mon 9/26/11	Fri 9/30/11	16																						
18	County Counsel ASAA Review/Approve	10 days	Mon 10/3/11	Mon 10/17/11	17																						
19	Negotiate ASAA	5 days	Tue 10/18/11	Mon 10/24/11	18																						
20	County Counsel Blue Review	5 days	Tue 10/25/11	Mon 10/31/11	19																						
21	BOS Approval of ASAA (includes Legistar and Approval Chain)	10 days	Tue 11/1/11	Tue 11/15/11	20																						
22	Environmental Consistency Documentation	99 days	Sun 5/15/11	Tue 10/4/11																							
23	County Counsel Environmental Consistency Review/Approve -	15 days	Sun 5/15/11	Mon 6/6/11	2																						
24	Environmental Assesment Required for Cultural Resources and	30 days	Tue 6/7/11	Tue 7/19/11	23																						
25	Prepare Environmental Addendum for the File	5 days	Wed 7/20/11	Tue 7/26/11	24																						
26	BOS Adoption of Addendum	1 day	Tue 10/4/11	Tue 10/4/11	25																						
27	Phase 1 Design and Construction	313 days	Thu 7/28/11	Fri 10/26/12																							
28	Revise Water Design (Original Approval Expired)	20 days	Tue 8/23/11	Tue 9/20/11	13																						
29	Submit Wet Utilities to EID	5 days	Wed 9/21/11	Tue 9/27/11	28																						
30	EID Review and Approval	40 days	Wed 9/28/11	Mon 11/28/11	29																						
31	EID Water Main Extension Agreement (Includes Fees & BOS A	40 days	Wed 9/28/11	Mon 11/28/11	29																						
32	EID Sewer Connection Agreement (Includes Fees & BOS Appr	40 days	Wed 9/28/11	Mon 11/28/11	29																						
33	Submit Dry Utilities to AT&T	5 days	Thu 7/28/11	Wed 8/3/11																							
34	AT&T Approval	40 days	Thu 8/4/11	Thu 9/29/11	33																						
35	Dry Utility Service Agreements (Includes Fees, Office Engineer,	60 days	Fri 9/30/11	Fri 12/30/11	34																						
36	PS&E Preparation (including road, utilities, and site preparation	50 days	Tue 11/29/11	Fri 2/10/12	35,31,32,34,6,11,2																						
37	Office Engineer/County Counsel Review & Approve	20 days	Mon 2/13/12	Mon 3/12/12	36																						
38	BOS Approval and Authorization to Advertise	15 days	Tue 3/13/12	Mon 4/2/12	25,37																						
39	Bidding Period	30 days	Tue 4/3/12	Mon 5/14/12	38																						
40	Bid Opening and Bid Review	10 days	Tue 5/15/12	Tue 5/29/12	39																						
41	BOS Award of Contract	10 days	Wed 5/30/12	Tue 6/12/12	40																						
42	Contract Execution	15 days	Wed 6/13/12	Tue 7/3/12	41																						
43	Construction	80 days	Thu 7/5/12	Fri 10/26/12	42																						

Project: West Slope Animal Shelter Nc
Date: Thu 9/22/11

Critical		Task		Baseline		Milestone		Project Summary		Deadline	
Critical Split		Split		Baseline Split		Summary Progress		External Tasks			
Critical Progress		Task Progress		Baseline Milestone		Summary		External Milestone			

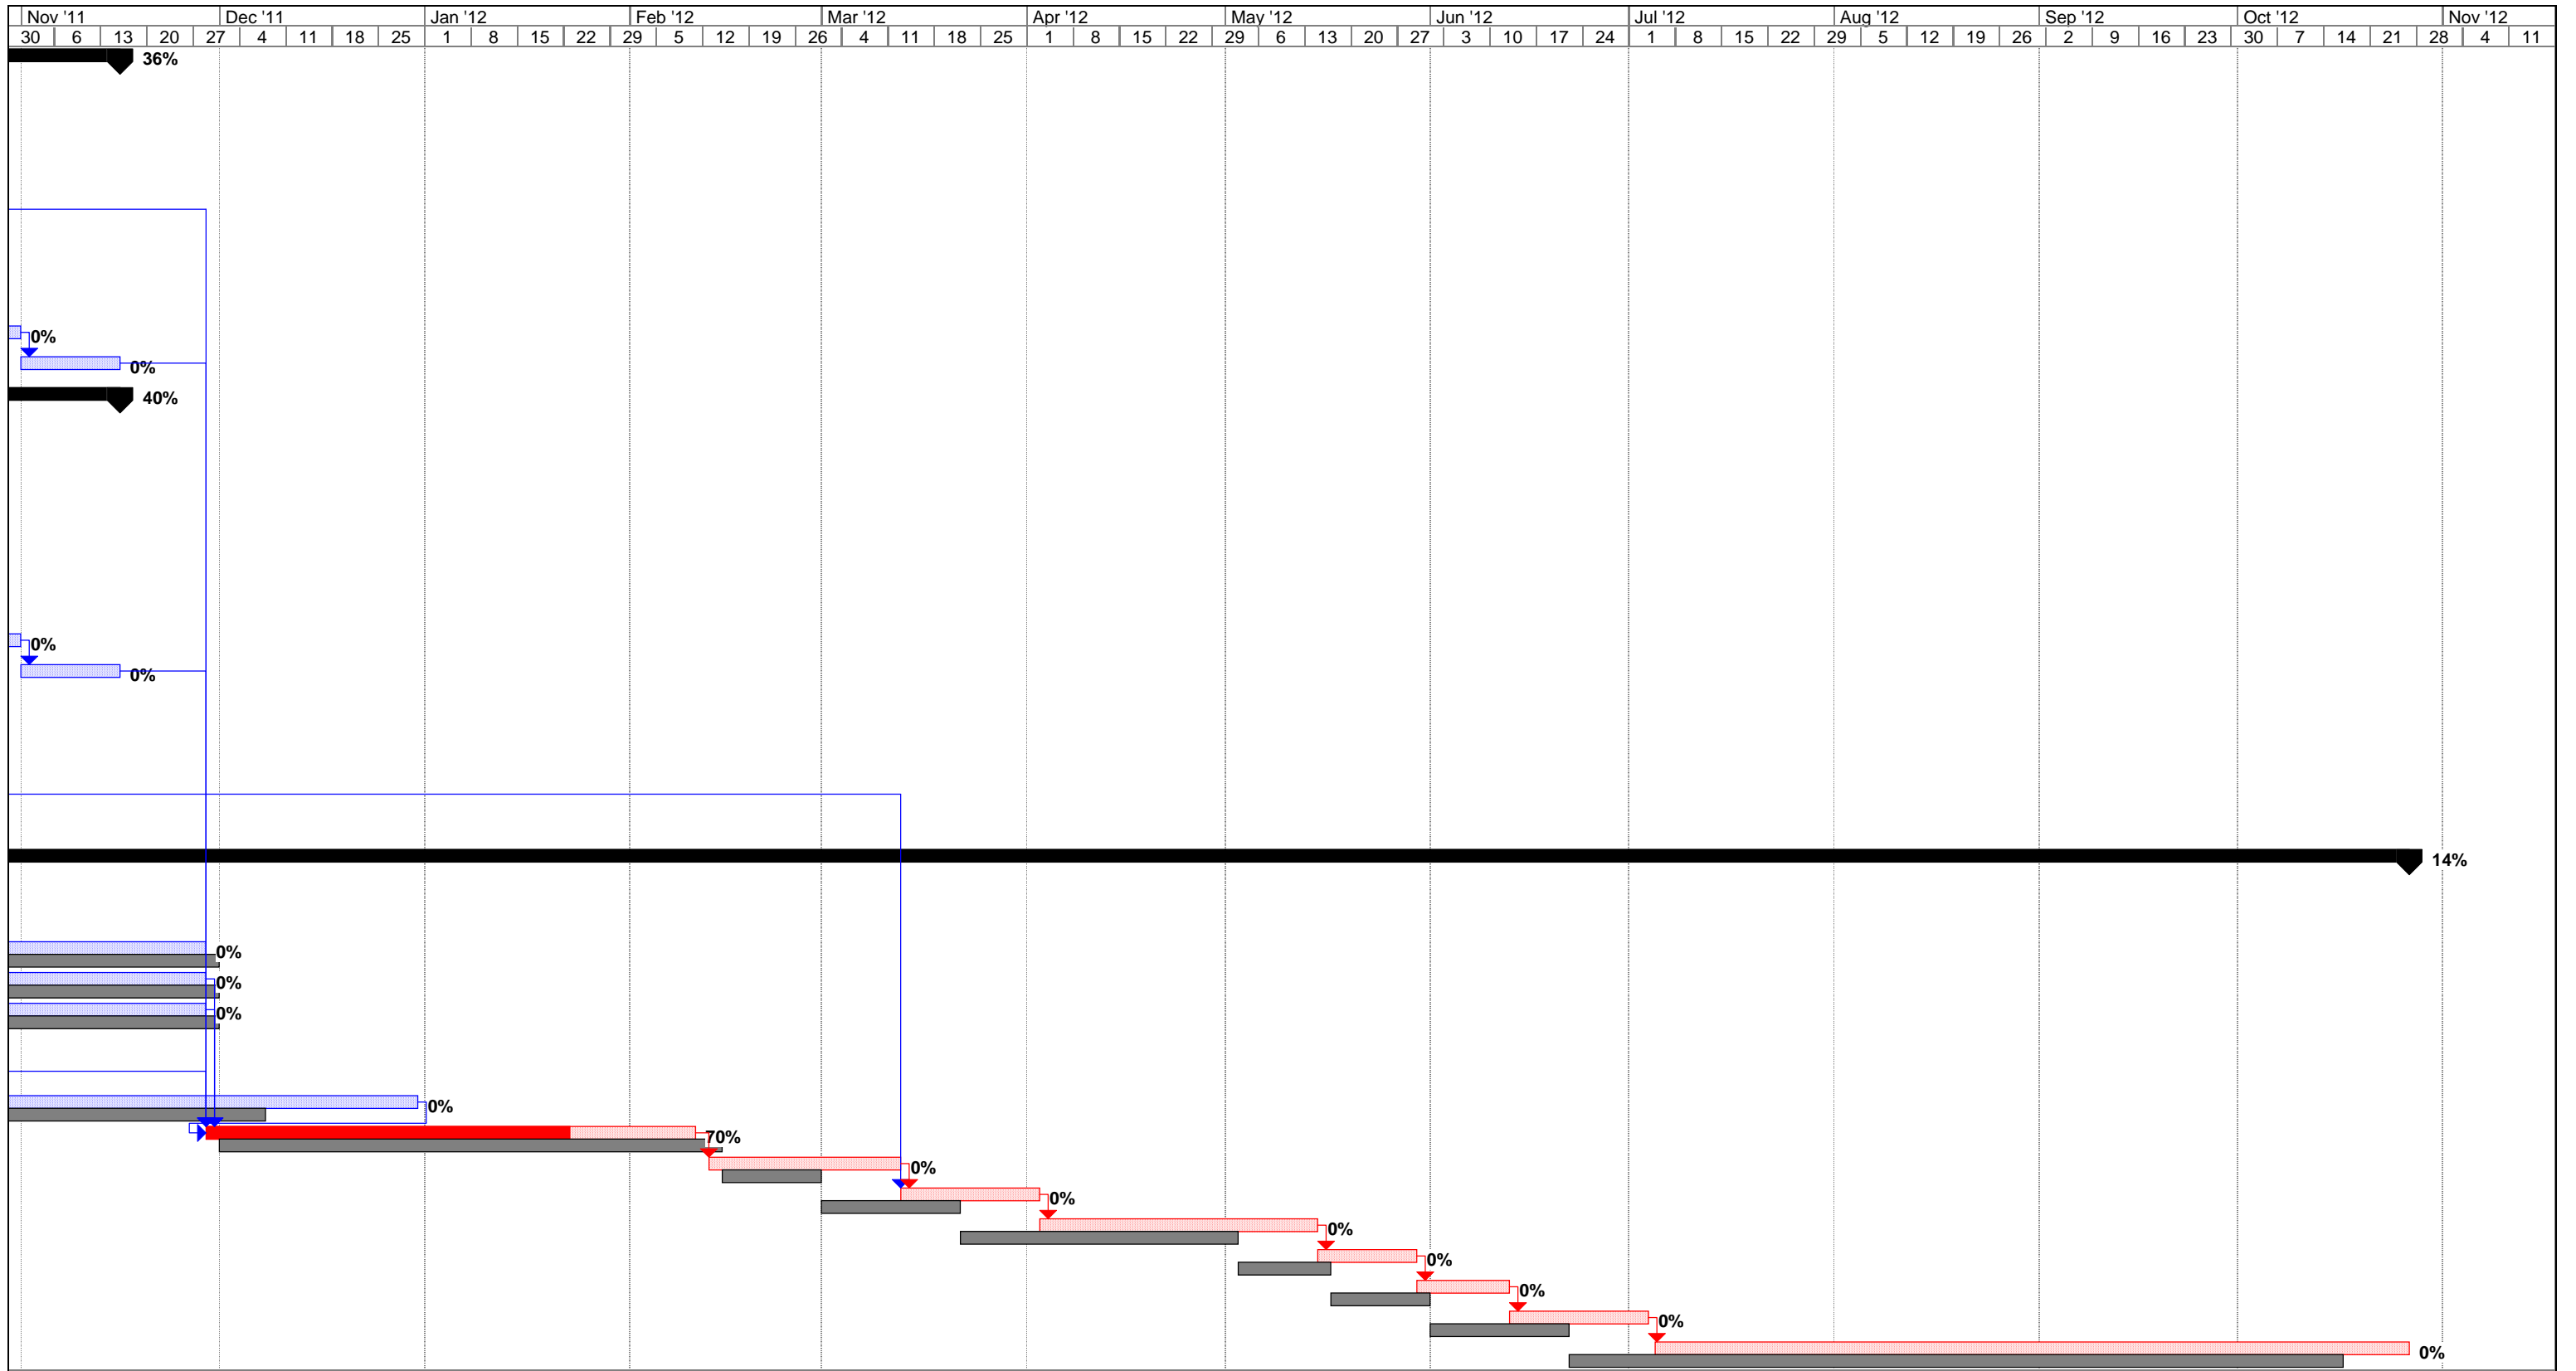


Project: West Slope Animal Shelter Nc
Date: Thu 9/22/11

Critical		Task		Baseline		Milestone		Project Summary		Deadline	
Critical Split		Split		Baseline Split		Summary Progress		External Tasks			
Critical Progress		Task Progress		Baseline Milestone		Summary		External Milestone			

ID	Task Name	Duration	Start	Finish	Predecessors	May				June				July				August				
						17	24	1	8	15	22	29	5	12	19	26	3	10	17	24	31	7
1																						
2	SHINN PURCHASE AGREEMENT AMENDMENT	141 days	Tue 4/26/11	Tue 11/15/11																		
3	ARCHITECTURAL SERVICES AGREEMENT AMENDMENT	131 days	Tue 5/10/11	Tue 11/15/11																		
4	Phase 2 Design and Construction	511 days	Tue 4/26/11	Mon 5/13/13																		
5	Define Scope of Work (includes Type Selection)	15 days	Tue 4/26/11	Mon 5/16/11																		
6	PS&E Preparation (including building and alternates)	80 days	Wed 11/16/11	Thu 3/15/12	5,3																	
7	Office Engineer Review/Approve	10 days	Fri 3/16/12	Thu 3/29/12	6																	
8	BOS Approval and Authorization to Advertise	30 days	Fri 3/30/12	Thu 5/10/12	3,7																	
9	Bidding Period	30 days	Fri 5/11/12	Fri 6/22/12	8																	
10	Bid Opening and Bid Review	15 days	Mon 6/25/12	Mon 7/16/12	9																	
11	BOS Award of Contract	10 days	Tue 7/17/12	Mon 7/30/12	10																	
12	Contract Execution	15 days	Tue 7/31/12	Mon 8/20/12	11																	
13	Construction	180 days	Tue 8/21/12	Mon 5/13/13	12																	

Project: West Slope Animal Shelter No Date: Tue 9/20/11	Critical		Split		Baseline Milestone		Project Summary	
	Critical Split		Task Progress		Milestone		External Tasks	
	Critical Progress		Baseline		Summary Progress		External Milestone	
	Task		Baseline Split		Summary		Deadline	

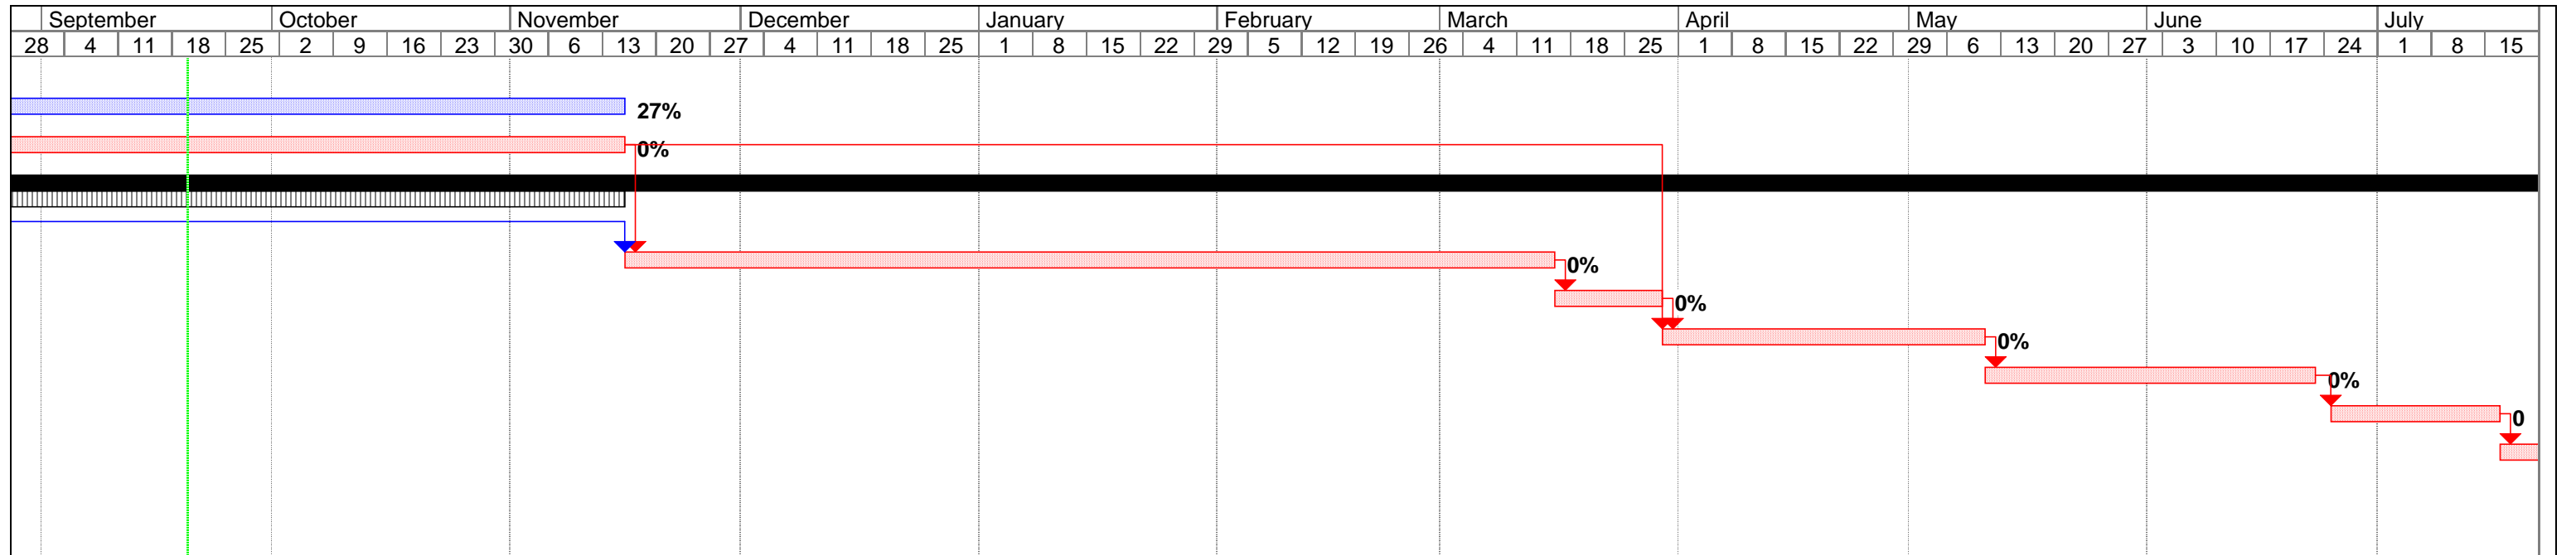


Project: West Slope Animal Shelter No
Date: Tue 9/20/11

- Critical
- Critical Split
- Critical Progress
- Task

- Split
- Task Progress
- Baseline
- Baseline Split

- Baseline Milestone
- Milestone
- Summary Progress
- Summary

- Project Summary
- External Tasks
- External Milestone
- Deadline

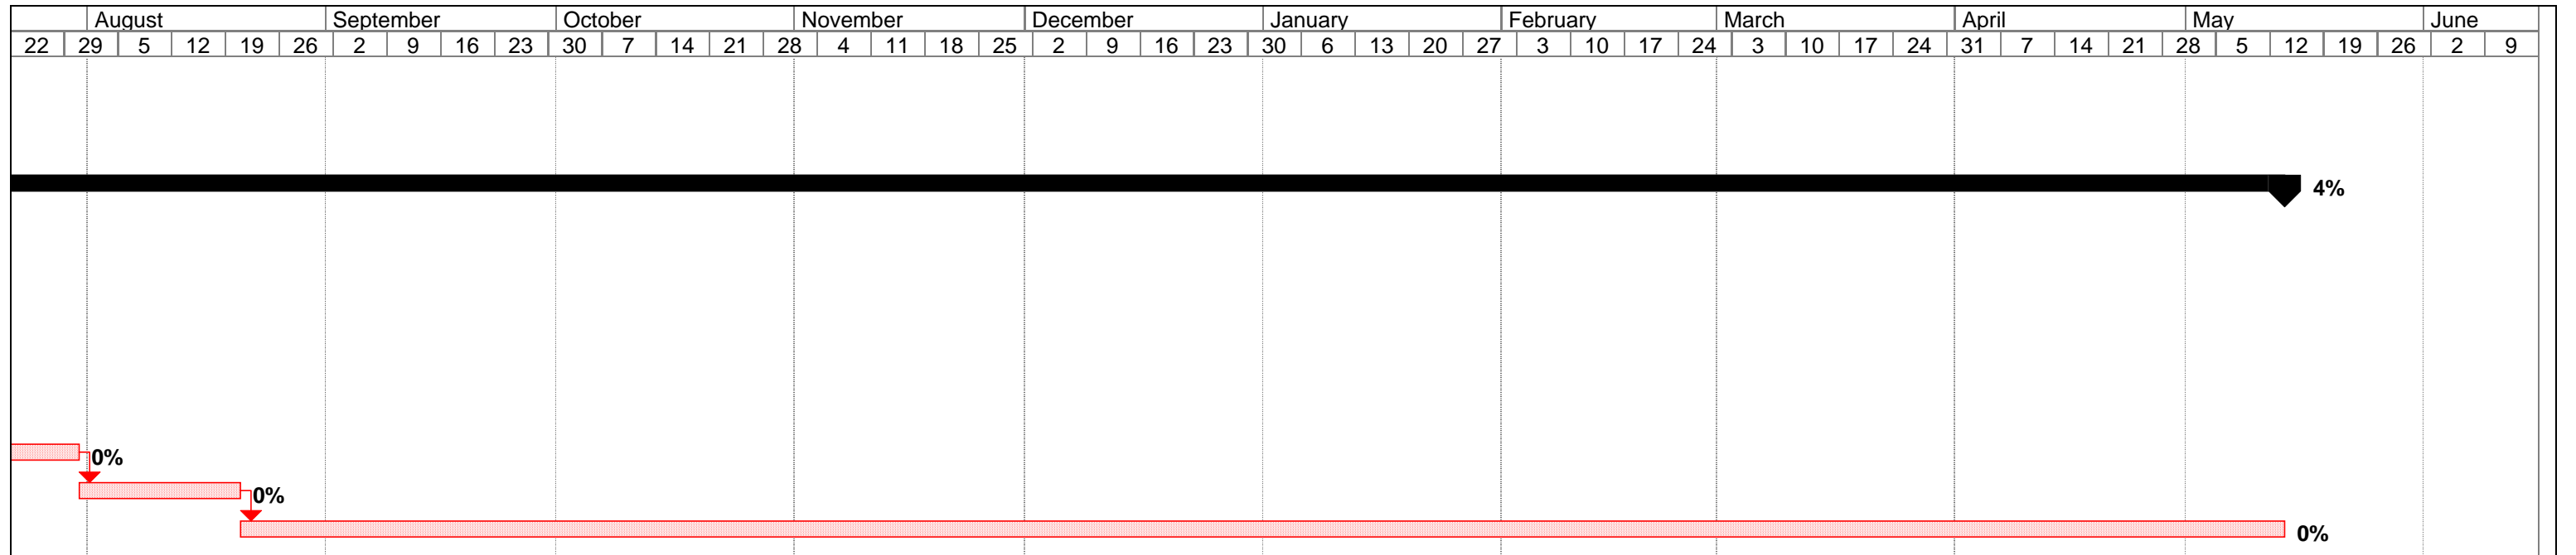

Project: West Slope Animal Shelter No
Date: Tue 9/20/11

Critical		Split		Baseline Milestone		Project Summary	
Critical Split		Task Progress		Milestone		External Tasks	
Critical Progress		Baseline		Summary Progress		External Milestone	
Task		Baseline Split		Summary		Deadline	
