

**ORIGINAL**

Agreement 03-0638  
Project No. 0314000039  
EA 4E620  
03-ED-50-21.95/24.45

**COOPERATIVE AGREEMENT COVER SHEET**

**Work Description**

CONSTRUCTION OF A MEDIAN BARRIER, UNDERCROSSING AND TRAFFIC  
MITIGATION ON US50 (PM 21.95/24.45)

**Contact Information**

**CALTRANS**

Clark Peri, Project Manager  
2379 Gateway Oaks Drive #150  
Sacramento, CA 95833  
Office Phone: (916) 825-8168  
Mobile Phone: (916) 825-8168  
Email: clark.peri@dot.ca.gov

**COUNTY OF EL DORADO**

Matt Smeltzer, Project Manager  
2850 Fairlane Court  
Placerville, CA 95667  
Office Phone: (530) 621-5912  
Email: matt.smeltzer@edcgov.us

## **COOPERATIVE AGREEMENT**

This AGREEMENT, effective on APRIL 4<sup>TH</sup>, 2019, is between the State of California, acting through its Department of Transportation, referred to as CALTRANS, and:

County of El Dorado, a political subdivision of the State of California, referred to hereinafter as COUNTY.

### **RECITALS**

1. PARTIES are authorized to enter into a cooperative agreement for improvements to the State Highway System per the California Streets and Highways Code, Sections 114 and 130.
2. For the purpose of this AGREEMENT, construction of a median barrier, undercrossing and traffic mitigation on US50 (PM 21.95/24.45) will be referred to hereinafter as PROJECT. The PROJECT scope of work is defined in the project initiation and approval documents (e.g. Project Study Report, Permit Engineering Evaluation Report, or Project Report).
3. All obligations and responsibilities assigned in this AGREEMENT to complete the following PROJECT COMPONENTS will be referred to hereinafter as WORK:
  - PLANS, SPECIFICATIONS, AND ESTIMATE (PS&E)
  - RIGHT-OF-WAY

Each PROJECT COMPONENT is defined in the CALTRANS Workplan Standards Guide as a distinct group of activities/products in the project planning and development process.

4. The term AGREEMENT, as used herein, includes this document and any attachments, exhibits, and amendments.

This AGREEMENT is separate from and does not modify or replace any other cooperative agreement or memorandum of understanding between the PARTIES regarding the PROJECT.

PARTIES intend this AGREEMENT to be their final expression that supersedes any oral understanding or writings pertaining to the WORK. The requirements of this AGREEMENT will preside over any conflicting requirements in any documents that are made an express part of this AGREEMENT.

If any provisions in this AGREEMENT are found by a court of competent jurisdiction to be, or are in fact, illegal, inoperative, or unenforceable, those provisions do not render any or all other AGREEMENT provisions invalid, inoperative, or unenforceable, and those provisions will be automatically severed from this AGREEMENT.

Except as otherwise provided in the AGREEMENT, PARTIES will execute a written amendment if there are any changes to the terms of this AGREEMENT.

PARTIES agree to sign a CLOSURE STATEMENT to terminate this AGREEMENT. However, all indemnification, document retention, audit, claims, environmental commitment, legal challenge, maintenance and ownership articles will remain in effect until terminated or modified in writing by mutual agreement or expire by the statute of limitations.

5. The following work associated with this PROJECT has been completed or is in progress:
  - CALTRANS approved the Categorical Exemption on August 1, 2016 (Cooperative Agreement No. 03-0583).
  - CALTRANS approved the Mitigated Negative Declaration on August 1, 2016 (Cooperative Agreement No. 03-0583).
6. In this AGREEMENT capitalized words represent defined terms, initialisms, or acronyms.
7. PARTIES hereby set forth the terms, covenants, and conditions of this AGREEMENT.

## **RESPONSIBILITIES**

### **Sponsorship**

8. A SPONSOR is responsible for establishing the scope of the PROJECT and securing the financial resources to fund the WORK. A SPONSOR is responsible for securing additional funds when necessary or implementing PROJECT changes to ensure the WORK can be completed with the funds obligated in this AGREEMENT.
9. CALTRANS is the SPONSOR for the WORK in this AGREEMENT.

### **Implementing Agency**

10. The IMPLEMENTING AGENCY is the PARTY responsible for managing the scope, cost, schedule, and quality of the work activities and products of a PROJECT COMPONENT.

- CALTRANS is the Plans, Specifications, and Estimate (PS&E) IMPLEMENTING AGENCY.

PS&E includes the development of the plans, specifications, and estimate; obtaining any resource agency permits; and the advertisement/award of the construction contract.

- CALTRANS is the RIGHT OF WAY IMPLEMENTING AGENCY

RIGHT OF WAY includes coordination with utility owners for the protection, removal, or relocation of utilities; the acquisition of right-of-way interests; and post-construction work such as right-of-way monumentation/recordation, relinquishments/vacations, and excess land transactions. The RIGHT OF WAY component budget identifies the cost of the capital costs of right-of-way acquisition (RIGHT-OF-WAY CAPITAL) and the cost of the staff work in support of the acquisition (RIGHT-OF-WAY SUPPORT).

11. Any PARTY responsible for completing WORK will make its personnel and consultants that prepare WORK available to help resolve WORK-related problems and changes for the entire duration of the PROJECT including PROJECT work that may occur under separate agreements.

## **Funding**

12. Funding sources, PARTIES committing funds, funding amounts, and invoicing/payment details are documented in the Funding Summary section of this AGREEMENT.

PARTIES will amend this AGREEMENT by updating and replacing the Funding Summary, in its entirety, each time the funding details change. Funding Summary replacements will be executed by a legally authorized representative of the respective PARTIES. The most current fully executed Funding Summary supersedes any previous Funding Summary created for this AGREEMENT.

13. PARTIES will not be reimbursed for costs beyond the funds obligated in this AGREEMENT.
14. Unless otherwise documented in the Funding Summary, overall liability for project costs within a PROJECT COMPONENT will be in proportion to the amount contributed to that PROJECT COMPONENT by each fund type.
15. Unless otherwise documented in the Funding Summary, any savings recognized within a PROJECT COMPONENT will be credited or reimbursed, when allowed by policy or law, in proportion to the amount contributed to that PROJECT COMPONENT by each fund type.
16. WORK costs, except those that are specifically excluded in this AGREEMENT, are to be paid from the funds obligated in the Funding Summary. Costs that are specifically excluded from the funds obligated in this AGREEMENT are to be paid by the PARTY incurring the costs from funds that are independent of this AGREEMENT.

## **CEQA/NEPA Lead Agency**

17. CALTRANS is the CEQA Lead Agency for the PROJECT.
18. FHWA is the NEPA Lead Agency for the PROJECT.

## **Environmental Permits, Approvals and Agreements**

19. PARTIES will comply with the commitments and conditions set forth in the environmental documentation, environmental permits, approvals, and applicable agreements as those commitments and conditions apply to each PARTY'S responsibilities in this AGREEMENT.
20. Unless otherwise assigned in this AGREEMENT, the IMPLEMENTING AGENCY for a PROJECT COMPONENT is responsible for all PROJECT COMPONENT WORK associated with coordinating, obtaining, implementing, renewing, and amending the PROJECT permits, agreements, and approvals whether they are identified in the planned project scope of work or become necessary in the course of completing the PROJECT.

21. The PROJECT requires the following environmental permits/approvals:

<b>ENVIRONMENTAL PERMITS/REQUIREMENTS</b>
404, US Army Corps Of Engineers
401, Regional Water Quality Control Board
National Pollutant Discharge Elimination System (NPDES), State Water Resources Control Board
1600 California Department of Fish and Wildlife

**Plans, Specifications, and Estimate (PS&E)**

22. As the PS&E IMPLEMENTING AGENCY, CALTRANS is responsible for all PS&E WORK except those activities and responsibilities that are assigned to another PARTY and those activities that are excluded under this AGREEMENT.
23. CALTRANS will prepare Utility Conflict Maps identifying the accommodation, protection, relocation, or removal of any existing utility facilities that conflict with construction of the PROJECT or that violate CALTRANS’ encroachment policy.
24. CALTRANS will determine the cost to positively identify and locate, accommodate, protect, relocate, or remove any utility facilities whether inside or outside the State Highway System right-of-way in accordance with federal and California laws and regulations, and CALTRANS’ policies, procedures, standards, practices, and applicable agreements including but not limited to Freeway Master Contracts.
25. PARTIES acknowledge that the activities Final District PS&E Package (255.20) and Contract Bid Documents “Ready to List” (260) will be performed by CALTRANS. Because CALTRANS is anticipated to perform the advertisement, award, and administration (AAA) of the construction contract, the PS&E package must be reviewed and approved by CALTRANS District and HQ Office Engineers prior to advertisement.

COUNTY will ensure that any consultant involved in the preparation of the PS&E package will remain available to address all comments generated during the performance of the Final District PS&E Package and Contract Bid Documents “Ready to List” activities.

**RIGHT-OF-WAY**

26. As the RIGHT-OF-WAY IMPLEMENTING AGENCY, CALTRANS is responsible for all RIGHT-OF-WAY WORK except those activities and responsibilities that are assigned to another PARTY and those activities that are excluded under this AGREEMENT.

27. CALTRANS will, using COUNTY contribution as shown in Funding Summary, purchase parcels, identified as “PROPOSED AREA TO BE ACQUIRED FOR COUNTY OF ED” in the attached Exhibit A, in the name of the COUNTY for County’s frontage road, which is part of this PROJECT. COUNTY agrees to accept title of these parcels.
28. COUNTY will secure all funds necessary in order for CALTRANS to purchase parcels in COUNTY’s name, as detailed in Exhibit A.
29. CALTRANS will cease all Right-of-Way work for parcels to be acquired in the COUNTY’s name if actual or expected R/W capital costs exceed funding obligations of the Funding Summary.
30. When RIGHT-OF-WAY is funded with State Transportation Improvement Program (STIP) funds, the acquisition of right-of-way will not occur prior to the approval of the environmental document by CALTRANS.
31. The California Transportation Commission is responsible for hearing and adopting Resolutions of Necessity.
32. CALTRANS will provide Right-of-Way Certification prior to PROJECT advertisement.
33. Physical and legal possession of the right-of-way must be completed prior to advertising the construction contract, unless PARTIES mutually agree to other arrangements in writing.
34. Right-of-way conveyances must be completed prior to WORK completion unless PARTIES mutually agree to other arrangements in writing.

### **Schedule**

35. PARTIES will manage the WORK schedule to ensure the timely use of obligated funds and to ensure compliance with any environmental permits, right-of-way agreements, construction contracts, and any other commitments. PARTIES will communicate schedule risks or changes as soon as they are identified and will actively manage and mitigate schedule risks.
36. The IMPLEMENTING AGENCY for each PROJECT COMPONENT will furnish PARTIES with a final report of the WORK completed.

## **Additional Provisions**

### **Standards**

37. PARTIES will perform all WORK in accordance with federal and California laws, regulations, and standards; Federal Highway Administration (FHWA) standards; and CALTRANS standards. CALTRANS standards include, but are not limited to, the guidance provided in the:
- CADD Users Manual
  - CALTRANS policies and directives
  - Plans Preparation Manual
  - Project Development Procedures Manual (PDPM)
  - Workplan Standards Guide
  - Standard Environmental Reference
  - Highway Design Manual
  - Right of Way Manual

### **Qualifications**

38. Each PARTY will ensure that personnel participating in WORK are appropriately qualified or licensed to perform the tasks assigned to them.
39. COUNTY will issue any encroachment permits that are necessary for WORK within its jurisdiction and outside the State Highway System right-of-way. COUNTY will provide encroachment permits to CALTRANS, its contractors, consultants and agents, at no cost.
40. The IMPLEMENTING AGENCY for a PROJECT COMPONENT will coordinate, prepare, obtain, implement, renew, and amend any encroachment permits needed to complete the WORK.

### **Protected Resources**

41. If any PARTY discovers unanticipated cultural, archaeological, paleontological, or other protected resources during WORK, all WORK in that area will stop and that PARTY will notify all PARTIES within 24 hours of discovery. WORK may only resume after a qualified professional has evaluated the nature and significance of the discovery and CALTRANS approves a plan for its removal or protection.



Disclosures

42. PARTIES will hold all administrative drafts and administrative final reports, studies, materials, and documentation relied upon, produced, created, or utilized for the WORK in confidence to the extent permitted by law and where applicable, the provisions of California Government Code, Section 6254.5(e) will protect the confidentiality of such documents in the event that said documents are shared between PARTIES.

PARTIES will not distribute, release, or share said documents with anyone other than employees, agents, and consultants who require access to complete the WORK without the written consent of the PARTY authorized to release them, unless required or authorized to do so by law.

43. If a PARTY receives a public records request pertaining to the WORK, that PARTY will notify PARTIES within five (5) working days of receipt and make PARTIES aware of any disclosed public documents. PARTIES will consult with each other prior to the release of any public documents related to the WORK.

Hazardous Materials

44. HM-1 is hazardous material (including, but not limited to, hazardous waste) that may require removal and disposal pursuant to federal or state law, irrespective of whether it is disturbed by the PROJECT or not.

HM-2 is hazardous material (including, but not limited to, hazardous waste) that may require removal and disposal pursuant to federal or state law only if disturbed by the PROJECT.

The management activities related to HM-1 and HM-2, including and without limitation, any necessary manifest requirements and disposal facility designations are referred to herein as HM-1 MANAGEMENT and HM-2 MANAGEMENT respectively.

45. If HM-1 or HM-2 is found, the discovering PARTY will immediately notify all other PARTIES.
46. CALTRANS, independent of the PROJECT, is responsible for any HM-1 found within the existing State Highway System right-of-way. CALTRANS will undertake, or cause to be undertaken, HM-1 MANAGEMENT with minimum impact to the PROJECT schedule.

CALTRANS will pay, or cause to be paid, the cost of HM-1 MANAGEMENT for HM-1 found within the existing State Highway System right-of-way with funds that are independent of the funds obligated in this AGREEMENT.

47. COUNTY, independent of the PROJECT, is responsible for any HM-1 found within the PROJECT limits and outside the existing State Highway System right-of-way. COUNTY will undertake, or cause to be undertaken, HM-1 MANAGEMENT with minimum impact to the PROJECT schedule.

COUNTY will pay, or cause to be paid, the cost of HM-1 MANAGEMENT for HM-1 found within the PROJECT limits and outside of the existing State Highway System right-of-way with funds that are independent of the funds obligated in this AGREEMENT.

48. The CONSTRUCTION IMPLEMENTING AGENCY is responsible for HM-2 MANAGEMENT within the PROJECT limits.
49. CALTRANS' acquisition or acceptance of title to any property on which any HM-1 or HM-2 is found will proceed in accordance with CALTRANS' policy on such acquisition.

#### Claims

50. Any PARTY that is responsible for completing WORK may accept, reject, compromise, settle, or litigate claims arising from the WORK without concurrence from the other PARTY.
51. PARTIES will confer on any claim that may affect the WORK or PARTIES' liability or responsibility under this AGREEMENT in order to retain resolution possibilities for potential future claims. No PARTY will prejudice the rights of another PARTY until after PARTIES confer on the claim.
52. If the WORK expends state or federal funds, each PARTY will comply with the Federal Uniform Administrative Requirements, Cost Principles, and Audit Requirements for Federal Awards of 2 CFR, Part 200. PARTIES will ensure that any for-profit consultant hired to participate in the WORK will comply with the requirements in 48 CFR, Chapter 1, Part 31. When state or federal funds are expended on the WORK, these principles and requirements apply to all funding types included in this AGREEMENT.

#### Accounting and Audits

53. PARTIES will maintain, and will ensure that any consultant hired by PARTIES to participate in WORK will maintain, a financial management system that conforms to Generally Accepted Accounting Principles (GAAP), and that can properly accumulate and segregate incurred PROJECT costs and billings.

54. PARTIES will maintain and make available to each other all WORK-related documents, including financial data, during the term of this AGREEMENT.

PARTIES will retain all WORK-related records for three (3) years after the final voucher.

PARTIES will require that any consultants hired to participate in the WORK will comply with this Article.

55. PARTIES have the right to audit each other in accordance with generally accepted governmental audit standards.

CALTRANS, the State Auditor, FHWA (if the PROJECT utilizes federal funds), and COUNTY will have access to all WORK-related records of each PARTY, and any consultant hired by a PARTY to participate in WORK, for audit, examination, excerpt, or transcription.

The examination of any records will take place in the offices and locations where said records are generated and/or stored and will be accomplished during reasonable hours of operation. The auditing PARTY will be permitted to make copies of any WORK-related records needed for the audit.

The audited PARTY will review the draft audit, findings, and recommendations, and provide written comments within thirty (30) calendar days of receipt.

Upon completion of the final audit, PARTIES have forty-five (45) calendar days to refund or invoice as necessary in order to satisfy the obligation of the audit.

Any audit dispute not resolved by PARTIES is subject to mediation. Mediation will follow the process described in the General Conditions section of this AGREEMENT.

56. If the WORK expends state or federal funds, each PARTY will undergo an annual audit in accordance with the Single Audit Act in the Federal Uniform Administrative Requirements, Cost Principles, and Audit Requirements for Federal Awards as defined in 2 CFR, Part 200.
57. When a PARTY reimburses a consultant for WORK with state or federal funds, the procurement of the consultant and the consultant overhead costs will be in accordance with the Local Assistance Procedures Manual, Chapter 10.

#### Interruption of Work

58. If WORK stops for any reason, each PARTY will continue with environmental commitments included in the environmental documentation, permits, agreements, or approvals that are in effect at the time that WORK stops, and will keep the PROJECT in environmental compliance until WORK resumes.

Penalties, Judgements and Settlements

59. The cost of awards, judgements, or settlements generated by the WORK are to be paid from the funds obligated in this AGREEMENT.
60. The cost of legal challenges to the environmental process or documentation may be paid from the funds obligated in this AGREEMENT.
61. Any PARTY whose action or lack of action causes the levy of fines, interest, or penalties will indemnify and hold all other PARTIES harmless per the terms of this AGREEMENT.

Environmental Compliance

62. If during performance of WORK additional activities or environmental documentation is necessary to keep the PROJECT in environmental compliance, PARTIES will amend this AGREEMENT to include completion of those additional tasks.

**GENERAL CONDITIONS**

**Venue**

63. PARTIES understand that this AGREEMENT is in accordance with and governed by the Constitution and laws of the State of California. This AGREEMENT will be enforceable in the State of California. Any PARTY initiating legal action arising from this AGREEMENT will file and maintain that legal action in the Superior Court of the county in which the CALTRANS district office that is signatory to this AGREEMENT resides, or in the Superior Court of the county in which the PROJECT is physically located.

**Exemptions**

64. All CALTRANS' obligations under this AGREEMENT are subject to the appropriation of resources by the Legislature, the State Budget Act authority, programming and allocation of funds by the California Transportation Commission (CTC).
65. PARTIES to this AGREEMENT recognize and acknowledge that COUNTY is a political subdivision of the State of California. As such, COUNTY is subject to the provisions of Article XVI, Section 18 of the California Constitution and other similar fiscal and procurement laws and regulations and may not expend funds not budgeted, or budgeted and then deleted from the budget for financial reasons, in a given fiscal year. All obligations of COUNTY under the terms of this agreement are subject to appropriation of funds in accordance with these requirements.

COUNTY utilizes grant funds and local discretionary funds collected each year to fund a portion of its obligations under this agreement and COUNTY's obligations are dependent on the receipt of said funds in a given year. Notwithstanding any other provision to the contrary, in the event that grant funds and local discretionary funds are insufficient to fund the COUNTY's obligations under this agreement, it shall not constitute an event of default, and COUNTY shall not be required to fund the obligation from any other funds or revenues, including but not limited to County General Fund. In that instance, COUNTY may request CALTRANS to stop PROJECT and meet with CALTRANS to negotiate and execute a formal written amendment to change the commitments made in this agreement.

### **Indemnification**

66. Neither CALTRANS nor any of their officers and employees, are responsible for any injury, damage, or liability occurring by reason of anything done or omitted to be done by COUNTY, its contractors, sub-contractors, and/or its agents under or in connection with any work, authority, or jurisdiction conferred upon COUNTY under this AGREEMENT. It is understood and agreed that COUNTY, to the extent permitted by law, will defend, indemnify, and save harmless CALTRANS and all of their officers and employees from all claims, suits, or actions of every name, kind, and description brought forth under, but not limited to, tortious, contractual, inverse condemnation, or other theories and assertions of liability occurring by reason of anything done or omitted to be done by COUNTY, its contractors, sub-contractors, and/or its agents under this AGREEMENT.
67. Neither COUNTY nor any of their officers and employees, are responsible for any injury, damage, or liability occurring by reason of anything done or omitted to be done by CALTRANS, its contractors, sub-contractors, and/or its agents under or in connection with any work, authority, or jurisdiction conferred upon CALTRANS under this AGREEMENT. It is understood and agreed that CALTRANS, to the extent permitted by law, will defend, indemnify, and save harmless COUNTY and all of their officers and employees from all claims, suits, or actions of every name, kind, and description brought forth under, but not limited to, tortious, contractual, inverse condemnation, or other theories and assertions of liability occurring by reason of anything done or omitted to be done by CALTRANS, its contractors, sub-contractors, and/or its agents under this AGREEMENT.

### **Non-parties**

68. PARTIES do not intend this AGREEMENT to create a third party beneficiary or define duties, obligations, or rights for entities not signatory to this AGREEMENT. PARTIES do not intend this AGREEMENT to affect their legal liability by imposing any standard of care for fulfilling the WORK different from the standards imposed by law.

69. PARTIES will not assign or attempt to assign obligations to entities not signatory to this AGREEMENT without an amendment to this AGREEMENT.

### **Ambiguity and Performance**

70. COUNTY will not interpret any ambiguity contained in this AGREEMENT against CALTRANS. COUNTY waives the provisions of California Civil Code, Section 1654.

A waiver of a PARTY's performance under this AGREEMENT will not constitute a continuous waiver of any other provision.

71. A delay or omission to exercise a right or power due to a default does not negate the use of that right or power in the future when deemed necessary.

### **Defaults**

72. If any PARTY defaults in its performance of the WORK, a non-defaulting PARTY will request in writing that the default be remedied within thirty (30) calendar days. If the defaulting PARTY fails to do so, the non-defaulting PARTY may initiate dispute resolution.

### **Dispute Resolution**

73. PARTIES will first attempt to resolve AGREEMENT disputes at the PROJECT team level as described in the Quality Management Plan. If they cannot resolve the dispute themselves, the CALTRANS District Director and the Executive Officer of COUNTY will attempt to negotiate a resolution. If PARTIES do not reach a resolution, PARTIES' legal counsel will initiate mediation. PARTIES agree to participate in mediation in good faith and will share equally in its costs.

Neither the dispute nor the mediation process relieves PARTIES from full and timely performance of the WORK in accordance with the terms of this AGREEMENT. However, if any PARTY stops fulfilling its obligations, any other PARTY may seek equitable relief to ensure that the WORK continues.

Except for equitable relief, no PARTY may file a civil complaint until after mediation, or forty-five (45) calendar days after filing the written mediation request, whichever occurs first.

PARTIES will file any civil complaints in the Superior Court of the county in which the CALTRANS District Office signatory to this AGREEMENT resides or in the Superior Court of the county in which the PROJECT is physically located.

74. PARTIES maintain the ability to pursue alternative or additional dispute remedies if a previously selected remedy does not achieve resolution.

### **Prevailing Wage**

75. When WORK falls within the Labor Code § 1720(a)(1) definition of "public works" in that it is construction, alteration, demolition, installation, or repair; or maintenance work under Labor Code § 1771, PARTIES will conform to the provisions of Labor Code §§ 1720-1815, and all applicable provisions of California Code of Regulations, Title 8, Division 1, Chapter 8, Subchapter 3, Articles 1-7. PARTIES will include prevailing wage requirements in contracts for public work and require contractors to include the same prevailing wage requirements in all subcontracts.

Work performed by a PARTY's own employees is exempt from the Labor Code's Prevailing Wage requirements.

If WORK is paid for, in whole or part, with federal funds and is of the type of work subject to federal prevailing wage requirements, PARTIES will conform to the provisions of the Davis-Bacon and Related Acts, 40 U.S.C. §§ 3141-3148.

When applicable, PARTIES will include federal prevailing wage requirements in contracts for public works. WORK performed by a PARTY's employees is exempt from federal prevailing wage requirements.

## **DEFINITIONS**

**PARTY** – Any individual signatory party to this AGREEMENT.

**PARTIES** – The term that collectively references all of the signatory agencies to this AGREEMENT.

**WORK BREAKDOWN STRUCTURE (WBS)** – A WBS is a standardized hierarchical listing of project work activities/products in increasing levels of detail. The CALTRANS WBS defines each **PROJECT COMPONENT** as a group of work activities/products. The CALTRANS WBS is defined in the CALTRANS Workplan Standards Guide.



**SIGNATURES**

PARTIES are empowered by California Streets and Highways Code to enter into this AGREEMENT and have delegated to the undersigned the authority to execute this AGREEMENT on behalf of the respective agencies and covenants to have followed all the necessary legal requirements to validly execute this AGREEMENT.

Signatories may execute this AGREEMENT through individual signature pages provided that each signature is an original. This AGREEMENT is not fully executed until all original signatures are attached.

**STATE OF CALIFORNIA  
DEPARTMENT OF TRANSPORTATION**




Nadarajah Suthahar  
Acting Deputy District Director  
District 3 Program / Project Management

APPROVED AS TO FORM:



Meera Danday  
Deputy Attorney

VERIFICATION OF FUNDS AND  
AUTHORITY:



District Project Control Officer

CERTIFIED AS TO FINANCIAL TERMS  
AND POLICIES:




Tamara Warren  
HQ Accounting Supervisor

**COUNTY OF EL DORADO**



Sue Novasel  
Chair, Board of Supervisors

ATTEST:



James S. Mitrison 4/2/2019  
Clerk of the Board of Supervisors

APPROVED AS TO FORM AND  
PROCEDURE:



Rafael Martinez  
Director, Department of Transportation

**FUNDING SUMMARY NO. 01**

<b><u>FUNDING TABLE</u></b> <span style="float: right;">v. 12</span>						
<u>IMPLEMENTING AGENCY</u> →			<u>CALTRANS</u>	<u>CALTRANS</u>		Totals
Source	Party	Fund Type	PS&E	R/W SUPPORT	R/W CAPITAL	
STATE	CALTRANS	SHOPP	3,500,000	1,200,000	3,000,000	7,700,000
LOCAL-FEDERAL	COUNTY	Urban-STBG <sup>T</sup>	0	0	950,000	950,000
Totals			3,500,000	1,200,000	3,950,000	8,650,000

<sup>T</sup>Toll Credits applied

<b><u>SPENDING SUMMARY</u></b> <span style="float: right;">v 221</span>						
Fund Type	<u>PS&amp;E</u>		<u>R/W Support</u>		<u>R/W CAPITAL</u>	Totals
	<u>CALTRANS</u>	<u>COUNTY</u>	<u>CALTRANS</u>	<u>COUNTY</u>	<u>CALTRANS</u>	
SHOPP	3,500,000	0	1,200,000	0	3,000,000	7,700,000
Urban-STBG	0	0	0	0	950,000	950,000
<b>Totals</b>	3,500,000	0	1,200,000	0	3,950,000	8,650,000

**Funding**

1. If there are insufficient funds available in this AGREEMENT to place the PROJECT right-of-way in a safe and operable condition, the appropriate IMPLEMENTING AGENCY will fund these activities until such time as PARTIES amend this AGREEMENT.

That IMPLEMENTING AGENCY may request reimbursement for these costs during the amendment process.

2. If there are insufficient funds in this AGREEMENT to implement the obligations and responsibilities of this AGREEMENT, including the applicable commitments and conditions included in the PROJECT environmental documentation, permits, agreements, and/or approvals that are in effect at a time that WORK stops, each PARTY accepts responsibility to fund their respective WORK until such time as PARTIES amend this AGREEMENT.

Each PARTY may request reimbursement for these costs during the amendment process.

**ICRP Rate**

3. The cost of any engineering support performed by CALTRANS includes all direct and applicable indirect costs. CALTRANS calculates indirect costs based solely on the type of funds used to pay support costs. State and federal funds administered by CALTRANS are subject to the current Program Functional Rate. All other funds are subject to the current Program Functional Rate and the current Administration Rate. The Program Functional Rate and Administration Rate are adjusted periodically.

In accordance with California Senate Bill 848, the Administration Rate is capped at 10 percent until July 1, 2021, for Self-Help Counties with a countywide sales tax measure dedicated to transportation improvements.

4. In accordance with the CALTRANS Federal-Aid Project Funding Guidelines, PARTIES must obtain approval from the Federal Highway Administration prior to any PROJECT funding changes that that will change the federal share of funds.

**Invoicing and Payment**

5. PARTIES will invoice for funds where the SPENDING SUMMARY shows that one PARTY provides funds for use by another PARTY. PARTIES will pay invoices within forty-five (45) calendar days of receipt of invoice when not paying with Electronic Funds Transfer (EFT). When paying with EFT, COUNTY will pay invoices within five (5) calendar days of receipt of invoice.
6. CALTRANS will draw from state and federal funds that are provided by COUNTY without invoicing COUNTY when CALTRANS administers those funds and CALTRANS has been allocated those funds by the CTC and whenever else possible.
7. When a PARTY is reimbursed for actual cost, invoices will be submitted each month for the prior month's expenditures. After all PROJECT COMPONENT WORK is complete, PARTIES will submit a final accounting of all PROJECT COMPONENT costs. Based on the final accounting, PARTIES will invoice or refund as necessary to satisfy the financial commitments of this AGREEMENT.

**Plans, Specifications, and Estimate (PS&E)**

8. No invoicing or reimbursement will occur for the PS&E PROJECT COMPONENT.

**RIGHT-OF-WAY Support**

9. No invoicing or reimbursement will occur for the R/W SUPPORT PROJECT COMPONENT.

**RIGHT-OF-WAY Capital**

10. No invoicing will occur for the R/W CAPITAL PROJECT COMPONENT. CALTRANS will encumber COUNTY's local-federal funds to fund actual costs incurred and paid for the parcels shown in attached Exhibit A. All costs associated with the identification and relocation of utilities will be covered by CALTRANS.

**CLOSURE STATEMENT INSTRUCTIONS**

1. Did PARTIES complete all scope, cost and schedule commitments included in this AGREEMENT and any amendments to this AGREEMENT?  

YES / NO
  
2. Did CALTRANS accept and approve all final deliverables submitted by other PARTIES?  

SAMPLES

YES / NO
  
3. Did the CALTRANS HQ Office of Accounting verify that all final accounting for this AGREEMENT and any amendments to this AGREEMENT were completed?  

YES / NO
  
4. If construction is involved, did the CALTRANS District Project Manager verify that all claims and third party billings (utilities, etc.) have been settled before termination of the AGREEMENT?  

YES / NO
  
5. Did PARTIES complete and transmit the As-Built Plans, Project History File, and all other required contract documents?  

YES / NO

If ALL answers are “YES”, this form may be used to TERMINATE this AGREEMENT.

**CLOSURE STATEMENT**

PARTIES agree that they have completed all scope, cost, and schedule commitments included in Agreement 03-0638 and any amendments to the agreement. The final signature date on this document terminates agreement 03-0638 except survival articles. All survival articles in agreement 03-0638 will remain in effect until expired by law, terminated or modified in writing by the PARTIES' mutual agreement, whichever occurs earlier.

The people signing this agreement have the authority to do so on behalf of their public agencies.

---

**CALTRANS**

\_\_\_\_\_  
Name  Date  
Deputy District Director, District 3 Program / Project Management

CERTIFIED AS TO ALL FINANCIAL OBLIGATIONS/TERMS AND POLICIES

\_\_\_\_\_  
Name Date  
District Project Control Officer

---



**COUNTY OF EL DORADO**

\_\_\_\_\_  
Name Date  
Chair, Board of Supervisors

NOTE: The State of California or its officers or agents shall not be responsible for the accuracy or completeness of digital images of this map.

# T10N R11E MDM SECTION 12

19 PM 3  
PARCEL 1  
043-030-27-100

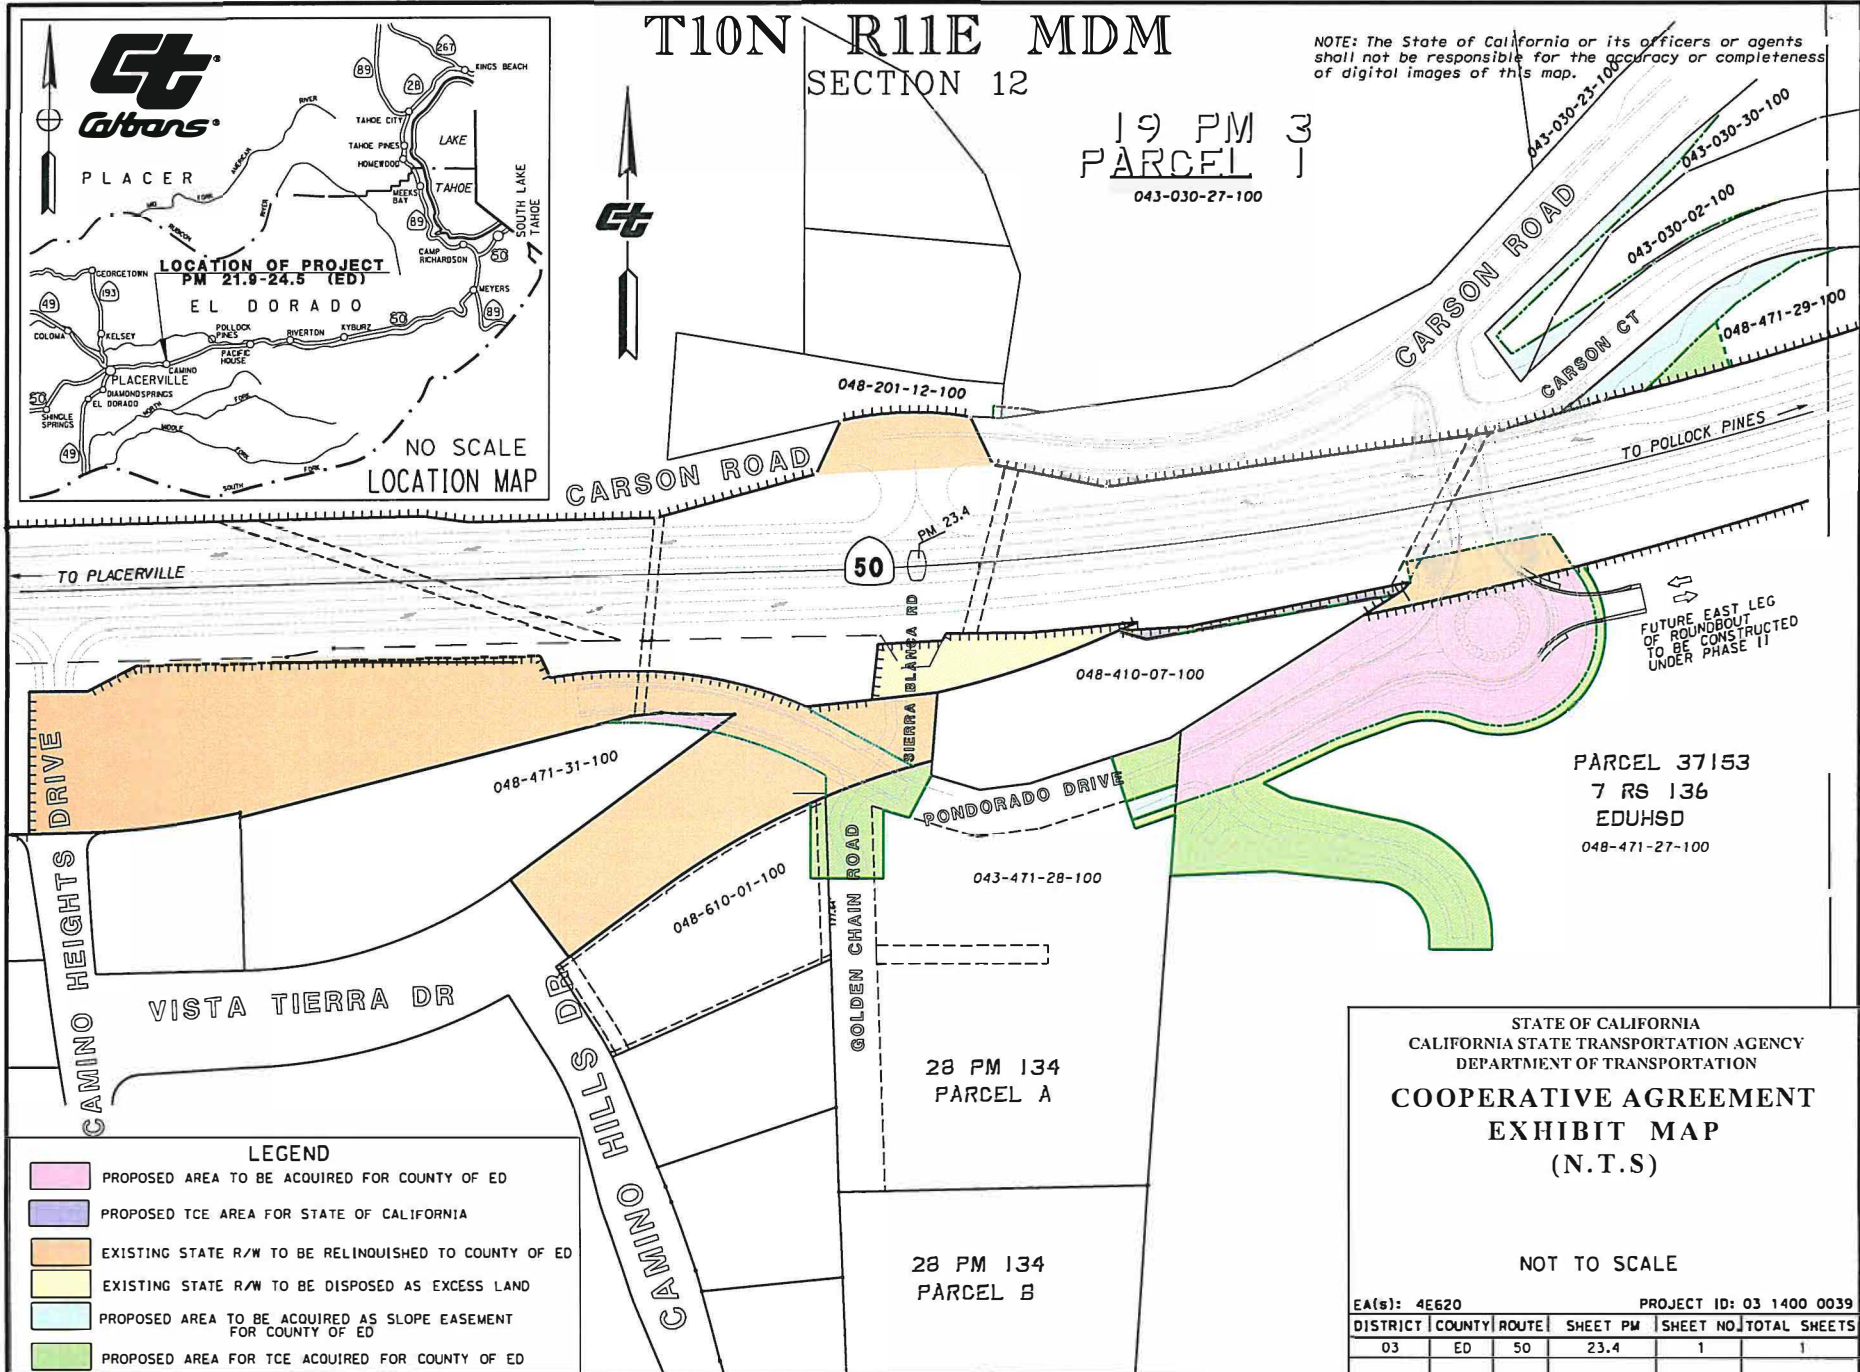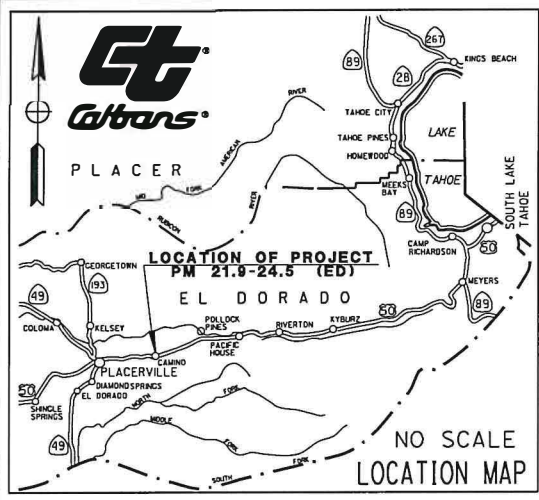

**LEGEND**

- PROPOSED AREA TO BE ACQUIRED FOR COUNTY OF ED
- PROPOSED TCE AREA FOR STATE OF CALIFORNIA
- EXISTING STATE R/W TO BE RELINQUISHED TO COUNTY OF ED
- EXISTING STATE R/W TO BE DISPOSED AS EXCESS LAND
- PROPOSED AREA TO BE ACQUIRED AS SLOPE EASEMENT FOR COUNTY OF ED
- PROPOSED AREA FOR TCE ACQUIRED FOR COUNTY OF ED

STATE OF CALIFORNIA  
CALIFORNIA STATE TRANSPORTATION AGENCY  
DEPARTMENT OF TRANSPORTATION

**COOPERATIVE AGREEMENT  
EXHIBIT MAP  
(N.T.S.)**

NOT TO SCALE

EA(s): 4E620 PROJECT ID: 03 1400 0039

DISTRICT	COUNTY	ROUTE	SHEET PM	SHEET NO	TOTAL SHEETS
03	ED	50	23.4	1	1
